



# Oswego Police Department

New Police Headquarters



## Blueprints for the Week

September 8, 2017

Editor – Deputy Chief Jim Jensen

Volume 2, Issue 1

### Photo of the Week



This "I" beam has been set into place and is being welded to the steel plate on the top of the brick. Crews will then fill in the beam pocket with additional block and grout.



### Video Clip of the Week

This week's video is another time-lapse, containing 12 hours of footage, condensed into a 2 minute clip. Click on the link below to view:

[https://youtu.be/Ht\\_CxfqXMwI](https://youtu.be/Ht_CxfqXMwI)

Comments or questions about this publication can be directed to Deputy Chief Jim Jensen.

**Oswego Police Department**  
3525 Route 34  
Oswego, Illinois 60543  
Phone: 630-551-7300  
Fax: 630-554-9379

### Steel, Steel and more Steel ...

Crews from AREA Erectors began working on the steel support beams and construction columns on the East end of the building. We could talk about how cool this is, but pictures are worth a thousand words! This week's edition is all about the STEEL.




Delivery



### Installation



This steel "I" beam slides right into the masonry pocket and is welded into place. A perfect fit!

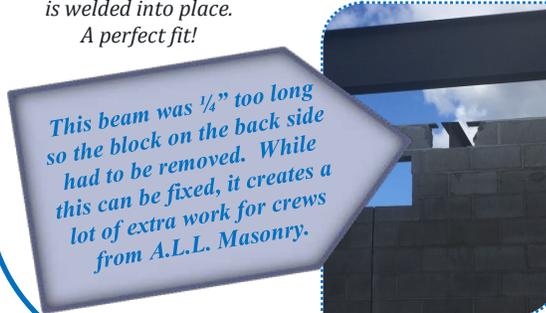

This beam was 1/4" too long so the block on the back side had to be removed. While this can be fixed, it creates a lot of extra work for crews from A.L.L. Masonry.



Steel roofing support beams in the Sally Port have been installed!

### Next Week

Work will continue on the steel support beams and construction columns. Additional crews will be installing the steel decking above the Sally Port and Holding Facility. Masonry crews have gradually worked their way around to the far West end of the training wing. Walls along the EOC and Defensive Tactics room have started and should be completed by the end of the week. Work will begin on the interior of the range floor this week with the excavation of the dirt and installation of the 36" diameter steel piping for the ranges ventilation system. The underground range work should be completed in two weeks.

### Long Term Goal

Gilbane's long term goal is to get the steel up and decking secured by the beginning of October. The exterior glazing (window) system will then begin, with the hope of getting the building envelope secured by the beginning of December.
