



# Oswego Police Department

New Police Headquarters



## Blueprints for the Week

August 31, 2018

Editor – Deputy Chief Jim Jensen


Volume 4, Issue 5

### Photo of the Week



#### Community Room

Crews from Bennett & Brouseau have continued installing the metal panels under the community room and on the tower with their focus next week on the entrance points into the building.



### Video Clip of the Week

In this week's time-lapse video, you will see that even the local geese like to walk around our property! The weather all week made outdoor activity very difficult, but crews continued to work outside as long as Mother Nature would allow it.

Click on the link below to view:



<https://youtu.be/zl38uE7f RE>




### Range Progress



Here is a sneak peek at the "before" and "middle".

In the coming weeks you will see the finished product.

Crews from Paragon have installed the noise reduction panels along the top of the concrete ceiling and framed out the rear air plenum wall. This week they started to hang the steel ceiling baffles along the south side of the range. These baffles are suspended in the air by chains that are mounted to a ceiling bracket. In the coming weeks you will see this range totally transform!

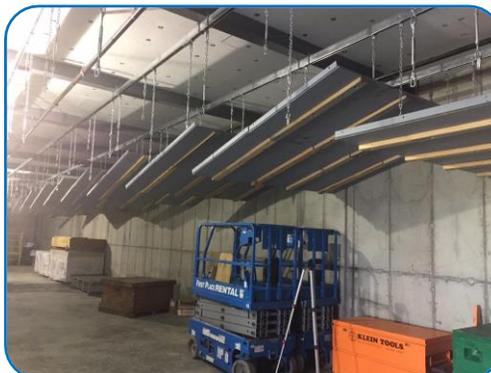


### Building Exterior


Exterior site work has been slow. The rain has put a damper on the parking lot and curb work. However, the design and bid of the exterior building signage (monument & wayfinding) has been completed. Quantum Sign Corporation out of Sugar Grove was awarded the exterior building sign package and has started work on the sign designs.



### Interior Photos

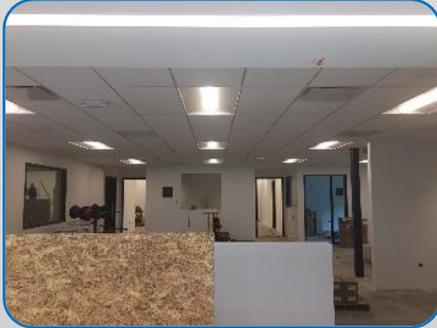

Ceiling

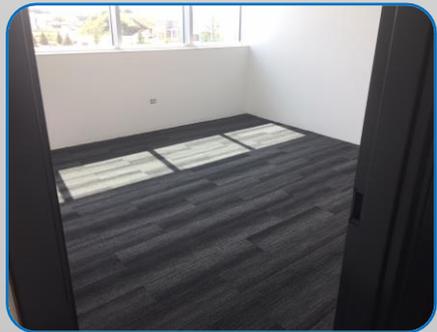

Deputy Chief's Office



Ceiling Baffles



Women's Locker Room

Comments or questions about this publication can be directed to Deputy Chief Jim Jensen.


**Oswego Police Department**  
3525 Route 34  
Oswego, Illinois 60543  
**Phone:** 630-551-7300  
**Fax:** 630-554-9379

### Building Interior

With two months left in the project there is a lot of work to be done. Crews have been working feverishly on finishing and programing the building mechanical units, installing the interior carpet, tile, millwork and cabinetry, completing final ceiling inspections and closing up the ceiling as well as completing the range construction. Interior wall construction in Records is also in progress with the reception counter lower wall and ballistic glazing installation. The photos on this page tell the story!



Lobby Tile Preparation

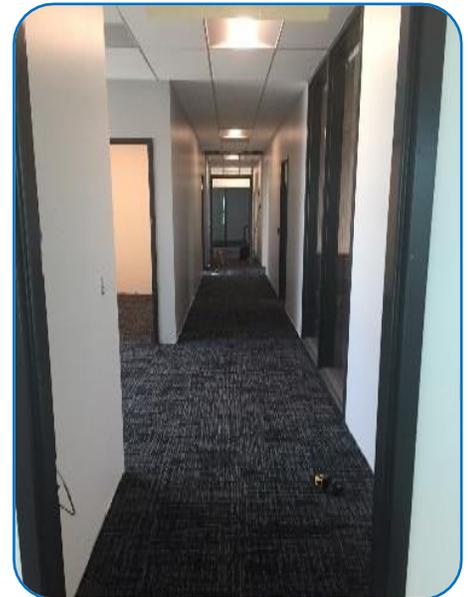

Administration Hallway



Reception Window  
Bullet Proof Glazing



Evidence Bag  
and Tag Area



Jail
