



# Oswego Police Department

## New Police Headquarters



# Blueprints for the Week

February 2, 2018


Editor – Deputy Chief Jim Jensen

Volume 3, Issue 4

### Photo of the Week



The stone wall along the training wing is complete. You will see the finished look once the metal panels are installed. The stone runs along the entire south wall of the training wing separated by glass enclosed "bump outs". These "bump outs" will act as break areas for staff during training days.



### Video Clip of the Week

This week's video is another time-lapse, containing 12 hours of footage, condensed into a 2 minute clip. You will see the Community Room glass being installed!

Click on the link below to view:


<https://youtu.be/07RfWITDnJ0>

Comments or questions about this publication can be directed to Deputy Chief Jim Jensen.

**Oswego Police Department**  
3525 Route 34  
Oswego, Illinois 60543  
**Phone:** 630-551-7300  
**Fax:** 630-554-9379

### Curtain Wall

Crews from Alliance Glazing continue to brave the cold and snow to install the curtain walls and set the glass. The curtain wall that surrounds the employee entrance is up and waiting for detailing and glass installation.

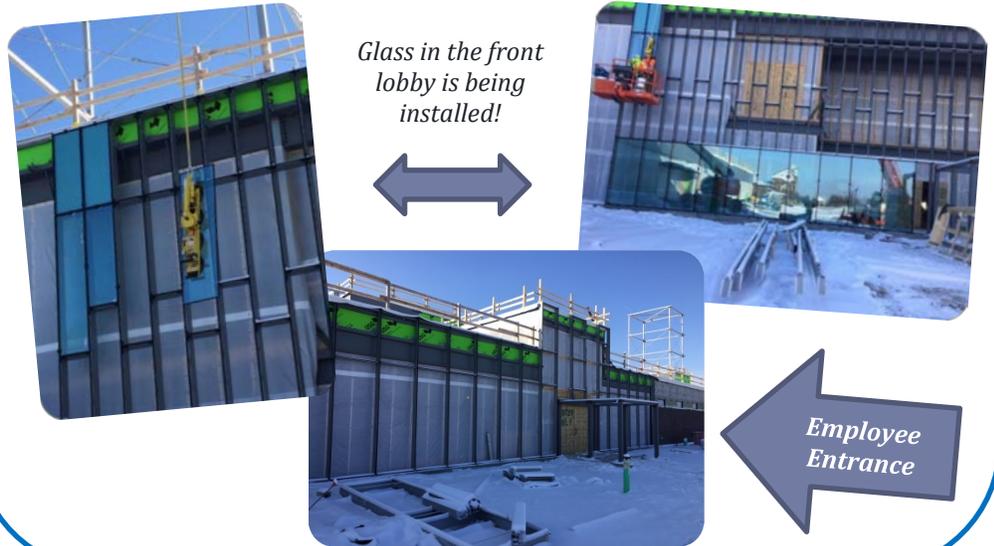


Glass in the front lobby is being installed!

Employee Entrance

### Interior

The second floor is really coming together! The interior walls are complete with crews continuing to set door and window frames. Champion Drywall is on site framing the window shade pockets that run along the South wall. These pockets will house the shades to keep the sun out.

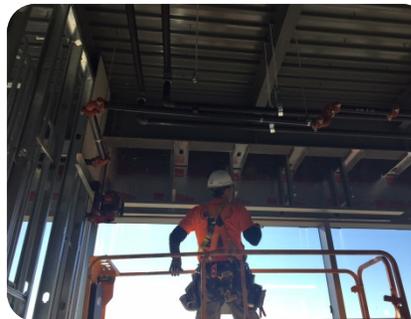

This picture shows some of the duct work on the main floor.

### Next Week

- Old Man Winter is wreaking havoc with the roofers, but interior work and the exterior curtain wall will continue.
- Alliance Glazing will hang over 100 individual panes of glass on the west lobby wall.
- Interior trades will continue to work on the second floor with drywall starting late next week!!

