



Oswego Police Department

New Police Headquarters



Blueprints for the Week

July 13, 2018

Editor – Deputy Chief Jim Jensen


Volume 4, Issue 1

Photo of the Week



Tower Construction Continues

Crews from Bennett & Brosseau have installed the West side corrugated metal framing and are almost finished installing the vertical mullions. Only three more sides to go! Next week you will see the guys from Acitelli installing the Evacuated Tube Solar Thermal System.



Video Clip of the Week

In this week's time-lapse video, you will witness the parking lot paving on the east side of the building. It's amazing to see what they can accomplish in a day!

Click on the link below to view:



<https://youtu.be/f9iI080EHn0>




Building Interior / Exterior

The Holding Facility is almost complete! This week crews finished the epoxy flooring. Once the steel security ceiling tiles are finished, the Holding Facility will be close to complete. There are a few small punch list items left to do, but that will be less than a day's work. The Holding Facility has 10 single cells and two 7-person holding cells. The open layout design was something that the architects (HOK) and the owner's rep (MWL) recommended and we feel it is perfect!



Flooring - BEFORE

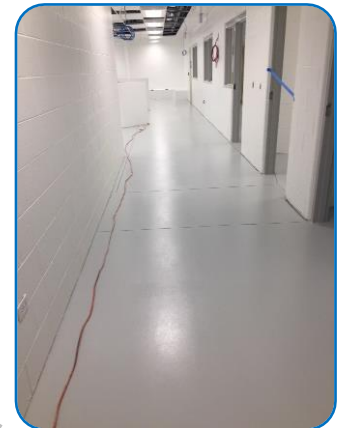

Finished Product

Interior Lighting – Excel Electric has completed the ceiling lights on a majority of the second floor. This has changed the entire look of each space! Final paint and carpet squares are next.

OPD Investigations unit will be working out of this area very soon!



Investigations Area



Range Mechanical Unit

Building Mechanicals – The five (5) mechanical units are in and installed. Crews are working hard to get these units ready to fire up. Two of the five units will be ready to go by the end of July. These units are enormous and require a lot of skilled work!






Records Counter



Records – Front Counter

Work has begun on the front Records counter. This is the area located just inside the main entrance.



Comments or questions about this publication can be directed to Deputy Chief Jim Jensen.

Oswego Police Department
3525 Route 34
Oswego, Illinois 60543
Phone: 630-551-7300
Fax: 630-554-9379

Site Work

Stone, asphalt base and the binder coat have been installed on the east side driveways and the north employee parking lot. This totally changes the look of the building and overall site!

BEFORE:



Roadway Layout

DURING:



North Parking Lot Gravel



Parking Lot Preparation

AFTER:



Binder Coat Paving



Employee Parking Lot Binder Coat

Next Week

Another busy week ahead:

- ❖ Crews from Abbey Paving will be prepping the West parking lot for curbs (and possibly gravel) by the end of the week.
- ❖ Kingston Tile will continue to lay the tile in the locker rooms and first floor bathrooms.
- ❖ The Holding Facility security ceiling should be completed by early next week, along with the detention door hardware and final connections.
- ❖ The final coat of paint on the second floor, along with carpet squares and cove base.
